




PUBLIC SAFETY BUILDING PROJECT



Weekly Project Updates and
7-Day Look-Ahead

**Here is a look-ahead at the construction work planned for the Public Safety Building,
from February 28, 2022 to March 4, 2022**

Project Overview:

Construction of a combined public safety building commenced in December 2020 on the site of the former Town Hall at 26 Bryant Street. The new building will house the staff and equipment of Fire, Police, and Dispatch departments. The new combined Public Safety Building will replace two older Town buildings: Police Station at 600 High Street (built in 1962) and the Fire Station at 436 Washington Street (built in 1930). The new building is scheduled to open in the Fall of 2022.

A [livestream video](#) of the construction is available on the Project website! Tune in from anywhere to watch the continued progress on the Combined Public Safety Building. While there, check out the updated Before-and-After photos of the progress onsite.

What to expect February 28, 2022 (Monday) through March 4, 2022 (Friday):

- The project site remains closed to the public.
- If additional snow removal efforts are needed, crews will be onsite **Saturday, February 26, 2022** to clear the site and remove snow.
- Roofing contractors will be working onsite this week to complete detail work.
- Crews will continue mechanical, electrical, fire protection, and plumbing installations this week.
- The build-out for the electrical/mechanical room within the building has begun and will continue this week.
- Repairs to the elevator shaft are expected to be completed this week. The anticipated delivery date of the elevator is **March 1, 2022**.
- The installation of the 4-inch concrete masonry unit wall in the garage is still underway. Masonry contractors will continue to install the stone veneer to the west side of the building this week.
- Installation of Stair #1 is anticipated to be completed by the end of the week.
- Eversource crews will return this week to relocate the existing overhead utility wires from the existing poles to the newly installed poles.
- The interior cold form metal framing work will continue this week. Air/vapor barrier installation is nearing completion and will continue this week.
- Crews will continue to install the exterior stone veneer on the east side of the building.
- Expect periodic entrance and exit of large trucks at the project site entrance, located at the intersection of Washington Street and Bryant Street. **Please expect minor traffic delays at this intersection.**
- No additional traffic impacts or pedestrian impacts are anticipated during this week.

Public Viewing Area:

If you want to stop by to check out the progress, stand by the picnic table outside the north entrance to Town Hall. This spot provides a great view into the project site and is outside of the project boundaries. Worth a visit!


Construction Hours:

- Crews will be onsite*:
 - Monday through Friday: 7:00 AM to 5:00 PM
 - *If crews need to remove snow on Saturday, February 26, 2022, they will be onsite 8:00 AM to 4:00 PM

Project Team Contact Information:

- Immediate issues or concerns, please contact the Town Manager's Office at [781-751-9100](tel:781-751-9100).
- For general questions or concerns, please contact the project team at psb@dedham-ma.gov
- For more information about the Public Safety Building Project, please visit the project website at www.dedham-ma.gov/psb
- Download our [project team contact information flyer](#) on the project website.

Click on the Before/After below to use the slider and enlarge

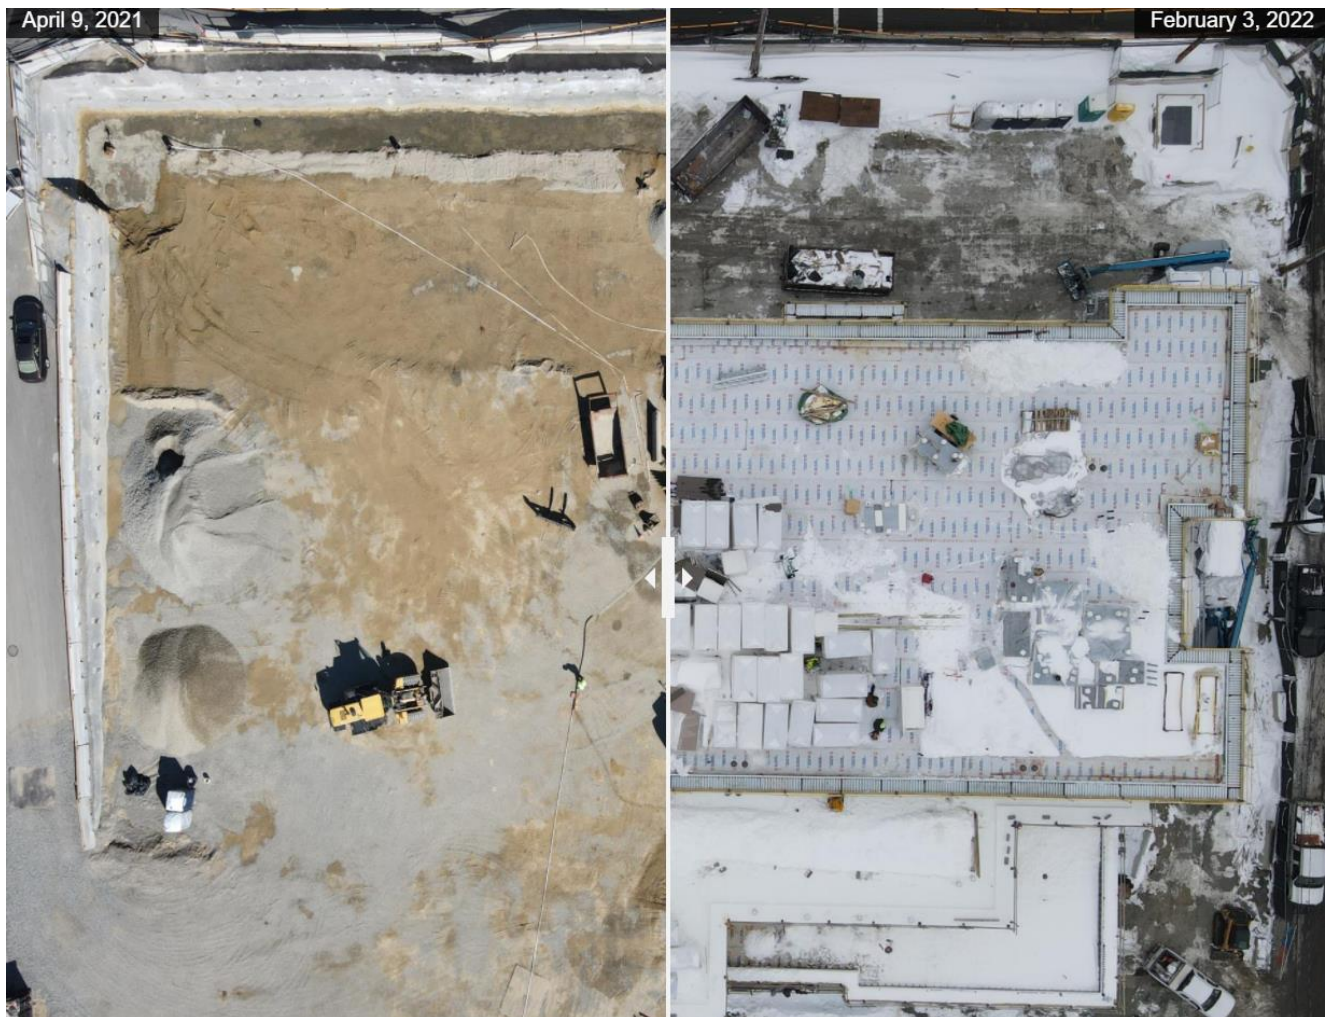

Caption: Aerial photos of the project site to show the progress of construction. The photo to the left was taken April 9, 2021, and the photo to the right was taken February 3, 2022. Both photos were taken by drone.

Note: To subscribe to the Public Safety Building Project e-mail notifications, [click here](#) to provide your name and email address.
