



Weekly Project Updates and 7-Day Look-Ahead

# Here is a look-ahead at the construction work planned for the Public Safety Building, from August 15, 2022 to August 19, 2022

#### **Project Overview:**

Construction of a combined public safety building commenced in December 2020 on the site of the former Town Hall at 26 Bryant Street. The new building will house the staff and equipment of Fire, Police, and Dispatch departments. The new combined Public Safety Building will replace two older Town buildings: Police Station at 600 High Street (built in 1962) and the Fire Station at 436 Washington Street (built in 1930). The new building is scheduled to open in the Fall of 2022.

A <u>livestream video</u> of the construction is available on the Project website! Tune in from anywhere to watch the continued progress on the Combined Public Safety Building. While there, check out the updated Before-and-After photos of the progress onsite.

## What to expect August 15, 2022 (Monday) through August 19, 2022 (Friday):

- The project site remains closed to the public.
- Contractors will be working onsite on **Saturday, August 13, 2022**, between 8:00 AM and 4:00 PM. All work will occur with the site boundaries and no vehicular or pedestrian impacts are anticipated.
- Installation of epoxy flooring will continue this week within the men's locker room on the second floor of the Fire Station.
- HVAC contractors will continue to install valves and associated piping for the inductions units located on the second floor of the Police Station. Additionally, contractors will be insulating the induction unit piping on the second floor of the Fire Station and will install a snow melt system along the north side of the building.
- Permanent power was supplied to the building on July 28, 2022 in anticipation of the generator. Delivery of the generator is pending, and an updated delivery date will be provided when available.
- Millwork installation is underway and will continue this week on the second floor of both Police and Fire Stations.
- Electrical contractors will continue to pull data wires to the second floor of both Police and Fire Stations, and crews will be installing more lights on the first floor of the Police Station.
- Painters will be working within the basement this week and will be painting the ceiling of the Apparatus Bay.
- Acoustic ceiling tile grid installation in the basement will occur this week.
- Metal parapet cap installation will continue this week along the east side of the building roof and along the Tower roof.
- Expect periodic entrance and exit of large trucks at the project site entrance, located at the intersection of Washington Street and Bryant Street. **Please expect minor traffic delays at this intersection.**
- No additional traffic impacts or pedestrian impacts are anticipated during this week.

#### **Public Viewing Area:**

If you want to stop by to check out the progress, stand by the picnic table outside the north entrance to Town Hall. This spot provides a great view into the project site and is outside of the project boundaries. Worth a visit!


#### **Construction Hours:**

- Crews will be onsite:
  - o Saturday, August 13, 2022: 8:00 AM to 4:00 PM
  - Monday through Friday: 7:00 AM to 5:00 PM

### **Project Team Contact Information:**


- Immediate issues or concerns, please contact the Town Manager's Office at <u>781-751-9100</u>.
- For general questions or concerns, please contact the project team at psb@dedham-ma.gov
- For more information about the Public Safety Building Project, please visit the project website at <a href="https://www.dedham-ma.gov/psb">www.dedham-ma.gov/psb</a>
- Download our project team contact information flyer on the project website.



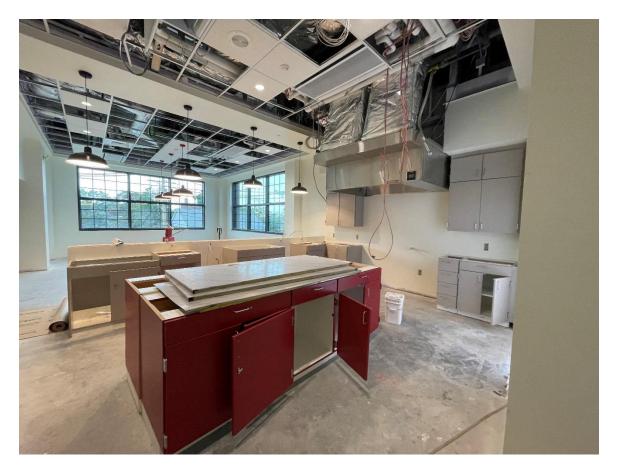

**Caption:** Photo of the cabinetry under construction within the Fire Station kitchen, taken on Thursday, August 11, 2022.

**Note:** To subscribe to the Public Safety Building Project e-mail notifications, <u>use this link</u> to enter you email address, and select "Public Safety Building" from the list of options.

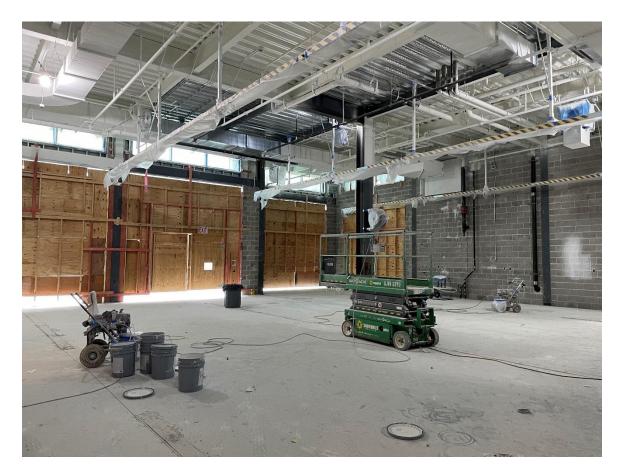

**Caption:** Photo of the ceiling painting underway in the Apparatus Bay, taken on Thursday, August 11, 2022.
