




PUBLIC SAFETY BUILDING PROJECT



Weekly Project Updates and
7-Day Look-Ahead

Here is a look-ahead at the construction work planned for the Public Safety Building, from August 9, 2021 to August 13, 2021

Project Overview:

Construction of a combined public safety building commenced in December 2020 on the site of the former Town Hall at 26 Bryant Street. The new building will house the staff and equipment of Fire, Police, and Dispatch departments. The new combined Public Safety Building will replace two older Town buildings: Police Station at 600 High Street (built in 1962) and the Fire Station at 436 Washington Street (built in 1930). The new building is scheduled to open in the Fall of 2022.

A [livestream video](#) of the construction is available on the Project website! Tune in from anywhere to watch the continued progress on the Combined Public Safety Building. While there, check out the updated Before-and-After photos of the progress onsite.

What to expect August 9, 2021 (Monday) through August 13, 2021 (Friday):

- The project site remains closed to the public.
- Crews will be working onsite on **Saturday, August 7, 2021, from 8:00 AM to 4:00 PM** to perform the following work: welding steel clips, installing decking, and detail work.
- The dewatering system remains in place and operational.
- Steel installation will continue using the crane located onsite.
- Deliveries of steel and metal decking will continue next week.
 - Expect periodic entrance and exit of large trucks at the project site entrance, located at the intersection of Washington Street and Bryant Street. **Please expect minor traffic delays at this intersection.**
- **Next week**, crews will continue to install waterproofing and damp proofing at the foundation walls.
- To maintain an efficient and organized jobsite, crews will continue to remove excess material for the site.
- No additional traffic impacts or pedestrian impacts are anticipated during this week.

Construction Hours:

- Crews will be working onsite on **Saturday, August 7 from 8:00 AM to 4:00 PM**. Trucks may be entering and exiting the site to remove material.
- Crews will be onsite next week, Monday through Friday, from 7:00 AM to 5:00 PM


Project Team Contact Information:

- Immediate issues or concerns, please contact the Dedham Town Manager's Office at [781-751-9100](tel:781-751-9100).
- For general questions or concerns, please contact the project team at psb@dedham-ma.gov
- For more information about the Public Safety Building Project, please visit the project website at www.dedham-ma.gov/psb
- Download our [project team contact information flyer](#) on the project website.

Click on the images below to enlarge



Caption: Drone photo of the project site taken on July 27, 2021, looking south. Installation of the concrete foundation walls are underway, and a delivery of metal decking is shown at the center of the photo.

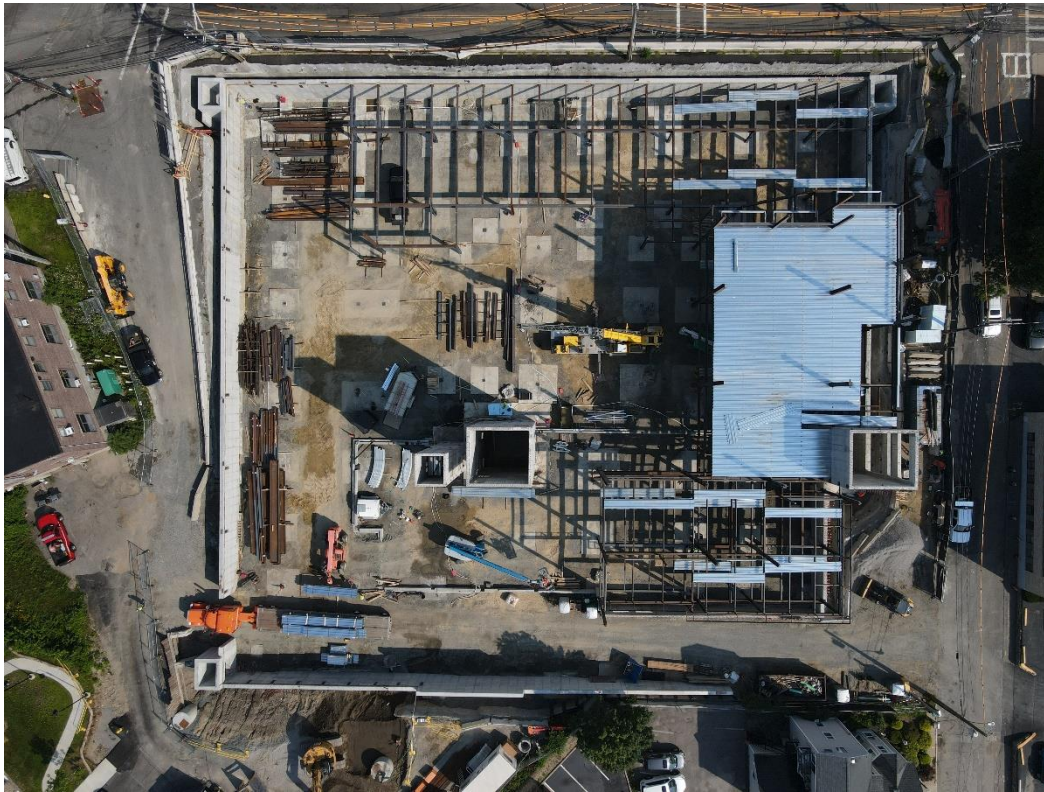

Caption: Aerial photo of construction site on July 27, 2021, by drone to show the layout of the steel beams installed so far, and the metal decking shown to the right.

Note: To subscribe to the Public Safety Building Project e-mail notifications, [click here](#) to provide your name and email address.
